


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	017	Qtr 3, 2017	Qtr 4, 2017	Qtr 1, 2018	Qtr 2, 2018	Qtr 3, 2018	Qtr 4, 2018	Qtr 1, 2019	Qtr 2, 2019	Qtr 3, 2019	Qtr 4, 2019	Qtr 1, 2020	
							Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
1		Scheme development	128 days?	Fri 01/09/17	Wed 28/02/18														
2		RIBA engaged	0 days	Fri 01/09/17	Fri 01/09/17														
3		Design competition developed	16 days?	Fri 08/09/17	Fri 29/09/17	2													
4		Design competition launched	0 days	Fri 29/09/17	Fri 29/09/17	3													
5		Design competition closes	0 days	Wed 31/01/18	Wed 31/01/18	4													
6		Design competition winners announced	0 days	Wed 28/02/18	Wed 28/02/18	5													
7		HE Funding	193 days?	Mon 03/07/17	Wed 28/03/18														
8		Value mangement	65 days?	Mon 03/07/17	Fri 29/09/17														
9		HE Gateway Approval	0 days	Tue 03/10/17	Tue 03/10/17	8													
10		Business case development (SAR)	97 days?	Tue 17/10/17	Wed 28/02/18	9FS+10 days													
11		Funding approval	0 days	Wed 28/03/18	Wed 28/03/18	10FS+20 days													
12		Design	160 days?	Thu 01/02/18	Wed 12/09/18														
13		Surveys (ground conditions etc)	20 days	Thu 01/02/18	Wed 28/02/18														
14		Outline design	40 days	Thu 01/03/18	Wed 25/04/18	13,6													
15		Detailed design	100 days	Thu 26/04/18	Wed 12/09/18	14													
16		Planning	101 days?	Wed 28/02/18	Wed 18/07/18														
17		Planning application developed	60 days	Wed 28/02/18	Tue 22/05/18	6													
18		Planning application submitted	0 days	Tue 22/05/18	Tue 22/05/18	17													
19		Planning application determined	1 day?	Wed 18/07/18	Wed 18/07/18	18FS+40 days													
20		Procurement	150 days	Mon 02/07/18	Fri 25/01/19														
21		Develop documentation	40 days	Mon 02/07/18	Fri 24/08/18														
22		Issue tender docs	0 days	Fri 24/08/18	Fri 24/08/18	21													
23		Tendering period	70 days	Mon 27/08/18	Fri 30/11/18	22													
24		Return of submissions	0 days	Fri 30/11/18	Fri 30/11/18	23													
25		Evaluation	20 days	Mon 03/12/18	Fri 28/12/18	24													
26		Award	0 days	Fri 25/01/19	Fri 25/01/19	25FS+20 days													
27		Construction	240 days	Fri 22/02/19	Fri 24/01/20														
28		Construction commences	0 days	Fri 22/02/19	Fri 22/02/19	26FS+20 days													
29		Construction	220 days	Mon 25/02/19	Fri 27/12/19	28													
30		Construction complete	0 days	Fri 24/01/20	Fri 24/01/20	29FS+20 days													

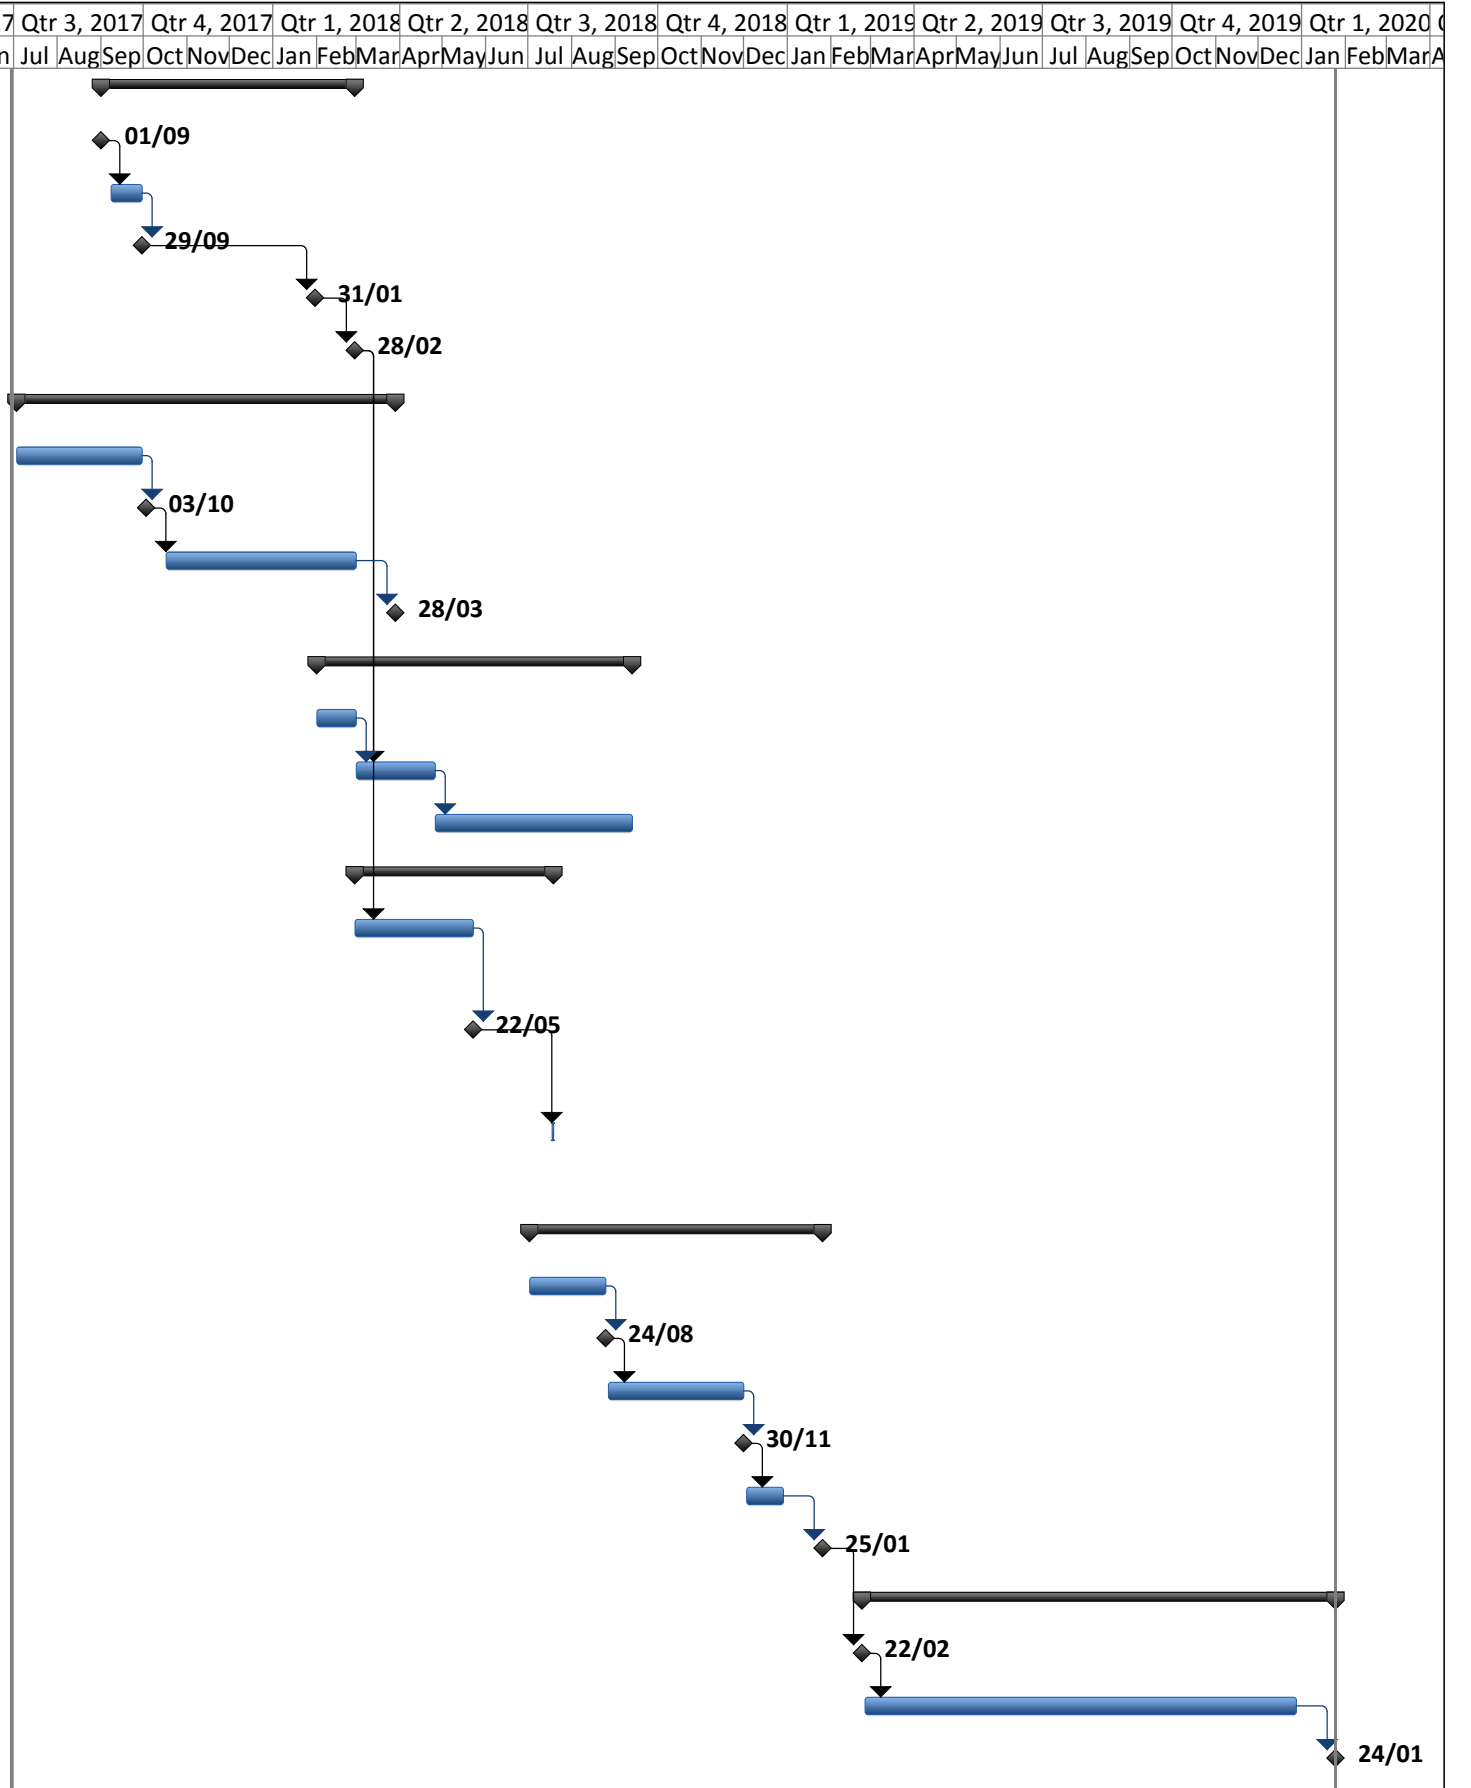

Project: Nexus25 cycle and footbr Date: Fri 30/06/17	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			
